

# Portaferry Public Realm Scheme


**Project Start Date: October 2023**  
**Project Completion Date: Summer 2024**  
**Project Value: £2M**

**Edition no: 9: 15/03/24**

**Welcome to the ninth newsletter for the Portaferry Public Realm Scheme.** Newsletters will be issued monthly as works progress to keep residents and businesses updated on progress and future work schedules. You can register to receive these newsletters by emailing 'SUBSCRIBE' to [portaferrypublicrealm@ardsandnorthdown.gov.uk](mailto:portaferrypublicrealm@ardsandnorthdown.gov.uk). Alternatively, printed newsletters will be delivered to Exploris, Portaferry Library and Portaferry Post Office and can be picked up from there by anyone interested in the scheme who does not have access to email.



*Works almost complete on the West footway*

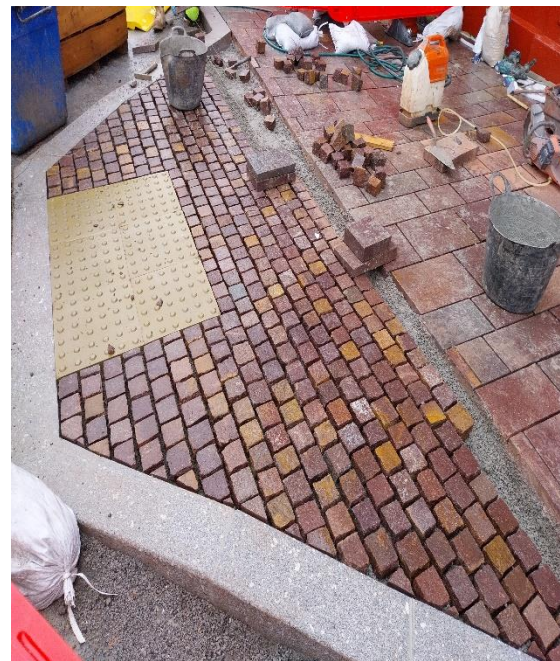

*Paving being laid at one of the crossing points*

For further information visit: [ardsandnorthdown.gov.uk/portaferrypublicrealm](https://ardsandnorthdown.gov.uk/portaferrypublicrealm)  
email: [portaferrypr@northstone-ni.com](mailto:portaferrypr@northstone-ni.com) or telephone: 07385 029 472  
24 Hour Contact No: 028 9039 4419

# Portaferry Public Realm Scheme

## CURRENT PLANNED WORKS

With the colder weather hopefully behind us, and the brighter mornings beginning, we are approaching the halfway mark with the Public Realm works.

The paving works are now completed along the West Footway heading towards the Church.

Northstone Ltd are currently laying the concrete base for the paving works within the Market Square and paving will start imminently. Over the next few weeks residents and businesses will begin to see the paving detail take shape within the Square.

Northstone's Civils Team have begun the footway works on the top of the scheme outside the Eurospar and pedestrian access to the footways will be maintained. These works will move from one side to the other to minimise disruption as much as possible.



## SEATING

With a laid-back style, the new seating to be installed in Market Square is designed to be inviting. It's sloping backrest conveys a feeling of relaxation, with an underlying strength in its serenity coming from the combination of hardwood slats and cast iron support.

For further information visit: [ardsandnorthdown.gov.uk/portaferrypublicrealm](https://ardsandnorthdown.gov.uk/portaferrypublicrealm)  
email: [portaferrypr@northstone-ni.com](mailto:portaferrypr@northstone-ni.com) or telephone: 07385 029 472  
24 Hour Contact No: 028 9039 4419

# Portaferry Public Realm Scheme

## Schedule of Works


The below schedule of works gives an idea of the proposed plan and dates of works in each area however please note that this is subject to change as the works commence. Keep an eye on the future newsletters and the website, [www.ardsandnorthdown.gov.uk/portaferrypublicrealm](http://www.ardsandnorthdown.gov.uk/portaferrypublicrealm) for regular updates on the planned works.

Phase 1 – Trial holes and Ferry Street **Oct 2023-Dec 2023**

Phase 2 – Castle Street **Nov 2023 – Feb 2024**

Phase 3 – Market Square and Junctions of Ferry St/The Strand & Castle St/The Strand **Jan 2024 – July 2024**

Phase 4 – Meetinghouse Street **June 2024-July 2024**

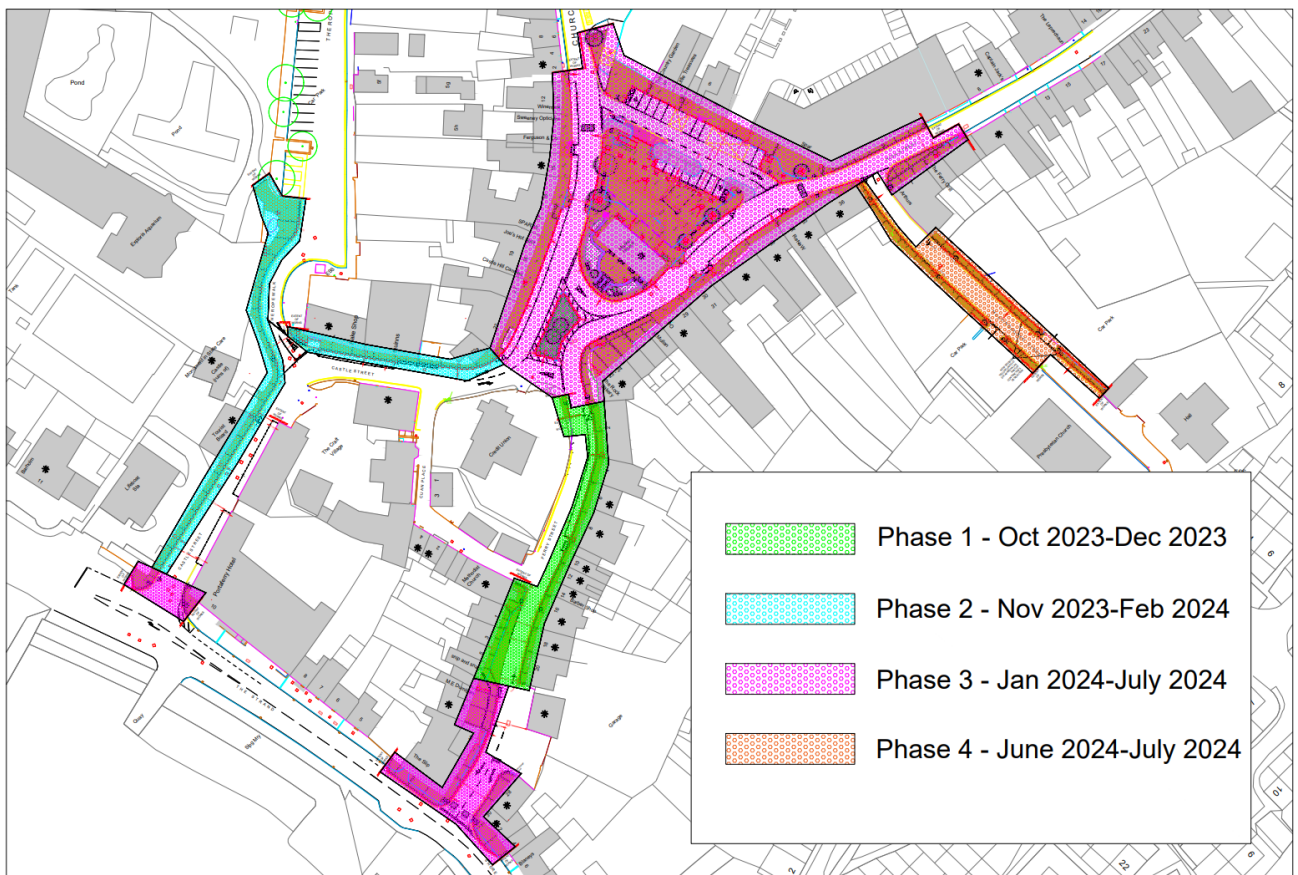

For further information visit: [ardsandnorthdown.gov.uk/portaferrypublicrealm](http://ardsandnorthdown.gov.uk/portaferrypublicrealm)  
email: [portaferrypr@northstone-ni.com](mailto:portaferrypr@northstone-ni.com) or telephone: 07385 029 472  
24 Hour Contact No: 028 9039 4419

# Portaferry Public Realm Scheme

## Scheme works

Widening of footpaths / Better pedestrian connectivity / Improved street lighting / Resurfacing footpaths with sustainable materials / The incorporation of street furniture / Planting / Re-designing the car park within Market Square to create a usable civic space

## Scope of scheme

Market Square / Castle Street / Ferry Street / High Street / Meeting House Street.

The Scheme Contractor, Northstone Ltd, will liaise with all of the residents and businesses within the scope of the scheme to try and reduce disruption during the period of works. Those traders and residents directly affected will be contacted by the contractor prior to works commencing.

## Contractor Contact Details

Northstone's Public Liaison Officer will be contactable on **07385029472** for any day-to-day queries about the works or particular requirements for access.

For out of hours contact, there is a 24hr contractor's contact number for Northstone: **02890394419**

Alternatively, there is a dedicated contractor's email address [portaferrypr@northstone-ni.com](mailto:portaferrypr@northstone-ni.com) where Northstone will endeavour to answer any queries or address any issues.



This project will greatly improve the village of Portaferry, enhancing the pavements and Market Square which will have long term benefits for residents and businesses. While we will endeavour to cause as little disruption as possible during our works, short delays and minor inconvenience are unavoidable and we would like to thank you in advance for your anticipated cooperation throughout our works.

The scheme is funded under the Covid Recovery Small Settlements Regeneration Programme (SSRP) with a contribution from Ards and North Down Borough Council. The SSRP is a collaborative approach, with contributions from the Department for Communities, Department for Infrastructure, and Department of Agriculture, Environment and Rural Affairs

For further information visit: [ardsandnorthdown.gov.uk/portaferrypublicrealm](https://ardsandnorthdown.gov.uk/portaferrypublicrealm)  
email: [portaferrypr@northstone-ni.com](mailto:portaferrypr@northstone-ni.com) or telephone: **07385 029 472**  
**24 Hour Contact No: 028 9039 4419**
